OHIO STATEWIDE AUTOMATED CHILD WELFARE INFORMATION SYSTEM (SACWIS)
REQUEST FOR PROPOSALS CONTRACT (#0A1292)
AMENDMENT 5

This Amendment 5 to contract #0A1292 (the "Amendment") is between the State of Ohio, Department of Administrative Services (the "State"), on behalf of the Ohio Department of Job and Family Services (ODJFS) (the "Agency"), and Deloitte Consulting LLP (the "Contractor"). This Amendment changes the terms of the contract named Ohio Statewide Automated Child Welfare Information System (SACWIS), #0A1292 (the "Contract").

WHEREAS, the State and Contractor entered into the Contract on May 19, 2022; and

WHEREAS, the State and Contractor determined that an amendment is necessary to address certain revisions to the Contract; and

WHEREAS, the State and Contractor determined that additional services are needed to address OHIO SACWIS' ability to respond to changing business needs and new policy requirements to include the Ohio Adoption Grant Program, described below.

Through House Bill 45, the Ohio Adoption Grant Program was created. This program aims to provide a one-time payment to parents who've adopted as of January 1st, 2023. Adoptive parents are potentially eligible to receive $10,000, adoptive foster parents potentially eligible to receive $15,000, and in some cases adoptive parents are eligible to receive $20,000 if the child has one or more special needs. To receive a grant payment, adoptive parents must have all of the following:

a) Had an adoption finalized on or after January 1, 2023;
b) Adopted a child under the age of 18;
c) Applied within one year of the adoption finalization;
d) Provided legal documentation proving adoption (final order of adoption, interlocutory order of adoption, or recognition of the adoption under R.C. section 3107.19); and
e) If applying for the special needs grant amount, provided documentation the child was diagnosed with one or more special needs as defined in division (G) of section 5101.19 of the Ohio Revised Code prior to the adoption finalization by a qualified professional.

NOW, THEREFORE, the Contract is amended as follows:

1. In Supplement 1, Scope of Work, of the Contract, Section 8.4 Systems Operations and Maintenance of ODJFS Child Welfare Systems Applications for the Ohio Adoption Grant Program Statement of Work below is added as a new section.

8.4 Systems Operations and Maintenance for ODJFS Child Welfare Systems Applications for the Ohio Adoption Grant Program Statement of Work

The JFS Office of Information Services (OIS) Salesforce team who implemented the adoptive parents' application portal will be available to the Contractor to provide technical guidance and responses to questions regarding the portal to enable the Contractor to complete the integration with Ohio SACWIS described below.

The Contractor must analyze and perform design activities necessary to extract data from the adoptive parents' application portal and integrate the portal with Ohio SACWIS which will allow for Office of Families and Children (OFC) staff to determine eligibility and issue payments. The Contractor will be responsible for design activities to enable conversion of applications into SACWIS, creation of Ohio Adoption Grant Program eligibility functionality within Ohio SACWIS,

creation of payment screens, and creation of payment interface batches to communicate payments from Ohio SACWIS to OFC.

Contractor must perform design activities for the following:

a. Integration of the adoptive parents' application portal with Ohio SACWIS to allow for OFC staff to determine eligibility and issue payments.
b. To facilitate extraction of the existing applications and place them into Ohio SACWIS during the integration process,
c. Creating eligibility functionality within Ohio SACWIS necessary to meet House Bill 45 requirements and any other requirements identified by OFC to implement the Ohio Adoption Grant Program,
d. Creating payment screens, and
e. Creating payment interface batches to communicate payments from Ohio SACWIS to OFIS.

It is estimated that 5,000 applications will need to be processed, annually, for this program. Applications to this program must be able to be submitted by April 6, 2023 and in the interim, payments will be processed manually. To fully operationalize this program, a system design is required to support the processing and payments related to incoming applications.

For purposes of estimating the effort for this section which includes program eligibility and payment functionality in Ohio SACWIS, the following assumptions were made regarding the work effect of this initiative:

1) Screens, (including business and security rules): 2 simple screens, 3 medium screens, 2 complex screens (eligibility review/exception processing, payment screens modifications)
2) Interfaces: 2 very complex (bidirectional interface between Ohio Grant Program site and Ohio SACWIS)
3) Batch Jobs: 3 complex, 1 medium, (new or modification to existing batch payments)
4) Reports: 1 simple, 2 medium, 2 complex (eligibility report, workload report, two payment reports, administrative report); note these reports will have to be done in FY24 if done by the c
5) Data Conversion: none
6) The requirement elaboration phase and design phase is being estimated and planned for, as well as the beginning of the technical design, with subsequent work being estimated in a future Change Request.

The assumptions listed above were used to drive the staffing estimates below. Both parties understand and agree that as additional information is realized during project execution, these assumptions will be reviewed and discussed. ODJFS and the Contractor agree that changes to these assumptions may not require a change order and both parties will work together to determine the impact to expected outcome and work.

The Contractor must provide staff, using the staff positions and rates established in the Contract, to provide the State a team focused on beginning the system implementation of the Ohio Adoption Grant Program. The following staff are estimated to support this initiative:

Staff Positions	FTE%
Business Analyst 2	100%
Business Analyst/Test Lead	150%
Integration Specialist	100%
Scrum Master	200%
Application Architect	100%


Technical Project Leader 50%

The Gantt chart below presents a high-level baseline schedule depicting the activities and timing for this work. Detailed requirement for deliverable tasks will be identified and documented during the design sessions. Once requirements are adequately documented, the tasks will be detailed in Application Lifecycle Management Quality Center and assigned specific release dates in the project schedule. The team will continually seek opportunities to synchronize work items to align resources efficiently across program activities.

Contractor understands Child Welfare is a dynamic field and that priorities may shift depending upon local business constraints, legislative changes, or state program and/or budget needs. Contractor must work actively with the State and other stakeholders to sequence deliverables and tasks to meet ODJFS priorities and improve service delivery; therefore, deliverables may be realigned if additional information is discovered during the design process, and it is agreed upon within the structure of the work.

ODJFS, Office of Families and Children
Ohio SACWIS Project Schedule

WBS#	Activity	Duration	Start	Finish	% Comple
0	OHIO SACWIS Project	273 days	8/1/22	8/16/23	51%
1	Start Project	0 days	9/1/22	9/1/22	0%
2	CR2: Start	122 days	9/1/22	2/17/23	100%
3	CR3: Start	273 days	8/1/22	8/16/23	37%
4	CR4 Start	112 days	12/1/22	5/5/23	32%
5	CR5 Start	93 days	4/3/23	8/9/23	0%
5.1	Ohio Adoption Grant Program (target 4.29 9/28/23 Prod deploy)	93 days	4/3/23	8/9/23	0%
5.1.1	Provide technical discovery and build services	65 days	4/3/23	6/30/23	0%
5.1.1.1	Discovery and Requirement Elaboration sessions	20 days	4/3/23	4/28/23	0%
5.1.1.2	Functional Designs	25 days	5/1/23	6/2/23	0%
5.1.1.3	Tech Approach	10 days	6/5/23	6/16/23	0%
5.1.1.4	Development	10 days	6/19/23	6/30/23	0%
5.1.2	Screen and Batch Specifications	83 days	4/17/23	8/9/23	0%
5.1.2.1	Screen and Batch Specifications DED	8 days	4/17/23	4/26/23	0%
5.1.2.1.1	Draft DED	3 days	4/17/23	4/19/23	0%
5.1.2.1.2	Submit DED	5 days	4/20/23	4/26/23	0%
5.1.2.1.3	Review/Approve DED	0 days	4/26/23	4/26/23	0%
5.1.2.2	Screen and Batch Specifications Deliverable	28 days	6/26/23	8/2/23	0%
5.1.2.2.1	Submit Deliverable	0 days	6/26/23	6/26/23	0%
5.1.2.2.2	Review Deliverable	23 days	6/26/23	7/26/23	0%
5.1.2.2.3	Revise/Finalize Deliverable	5 days	7/27/23	8/2/23	0%
5.1.2.2.4	Approve Deliverable	0 days	8/2/23	8/2/23	0%

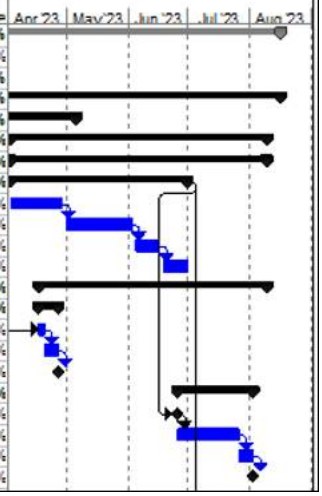

2. In Attachment Nine, Cost Summary, of the Contract, add a new tab titled “Amendment 5” for the work described in Section 8.4, including a not to exceed cost of $593,502.00. The revised Cost Summary, Attachment Nine, Cost Summary, Amendment 5, is incorporated into the Contract as if fully rewritten herein and is effective as of the effective date of this Amendment.

This Amendment shall become effective as of the date of the State’s signature and shall remain in full force and effect for the term of the Contract. Except as modified by this Amendment, all other terms, conditions, and pricing of the Contract shall remain the same and in full force and effect.

IN WITNESS WHEREOF, the parties have executed this Amendment as of the dates appearing below.

DELOITTE CONSULTING LLP

By: _____

Name: E-SIGNED by David Doyle on 2023-06-21 13:32:37 GMT

Title: _____

Date: _____

STATE OF OHIO
DEPARTMENT OF ADMINISTRATIVE SERVICES

By: E-SIGNED by Kathleen C. Madden /RLG on 2023-06-21 13:56:17 GMT

Name: Kathleen C. Madden

Title: Director

Date: _____

SUMMARY OF AMENDMENTS

Amendment Number	Effective Date	Description
5	In Progress	This Amendment 5 is to add Ohio Adoption Grant Program to the contract. The cost for this Amendment 5 is a total of $593,502.00
4	1/5/2023	This Amendment 4 is to add Tiered Foster Care to the contract. The cost for this Amendment 4 is a total of $461,982.00
3	1/5/2023	This Amendment 3 is to add an additional SOW for FY23. The cost for this Amendment 3 is a total of $2,337,801.00.
2	9/12/2022	This Amendment 2 is to setup the initial SOW for FY23. The cost for this Amendment 2 is a total of $1,469,937.00.
1	8/30/2022	This Amendment 1 is to correct a typo on the Contract One-pager document.
